NCC LIMITED

WHITE TOPPING YELAHANKA FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO AROMA BAKERY JUNCTION

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra Cafe To Kanti Sweets - LHS & RHS

Chainage : -

RMC Concrete : -

Grade of Concrete : M20

DATE OF CASTING : 26/2/2024

DATE OF TESTING : 05/3/2024

DATE OF TESTING : 26/3/2024

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS 516 /1959 and the results are Tabulated below.

Sl.No	Quantity in 'Cum'	Samples of Cubes NO's	7 Days				28 Days				Remarks
			Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	
01	35	6	8.31	360.2	16.01	17.00	8.50	518.02	23.03	23.95	
			8.40	3825	17.00		8.48	548.2	24.36		
			8.43	405.3	18.01		8.36	550.6	24.47		

AGENCY PMC AE BBMP AGENCY PMC AE BBMP

Infra Support Engineering Consultants P. Ltd. Bangaluru

Asst. Executive Engineer Project Division Yelahanka Zone BBMP, Bangalore - 92

Asst. Executive Engineer Project Division Yelahanka Zone BBMP, Bangalore - 92

Scanned by TapScanner

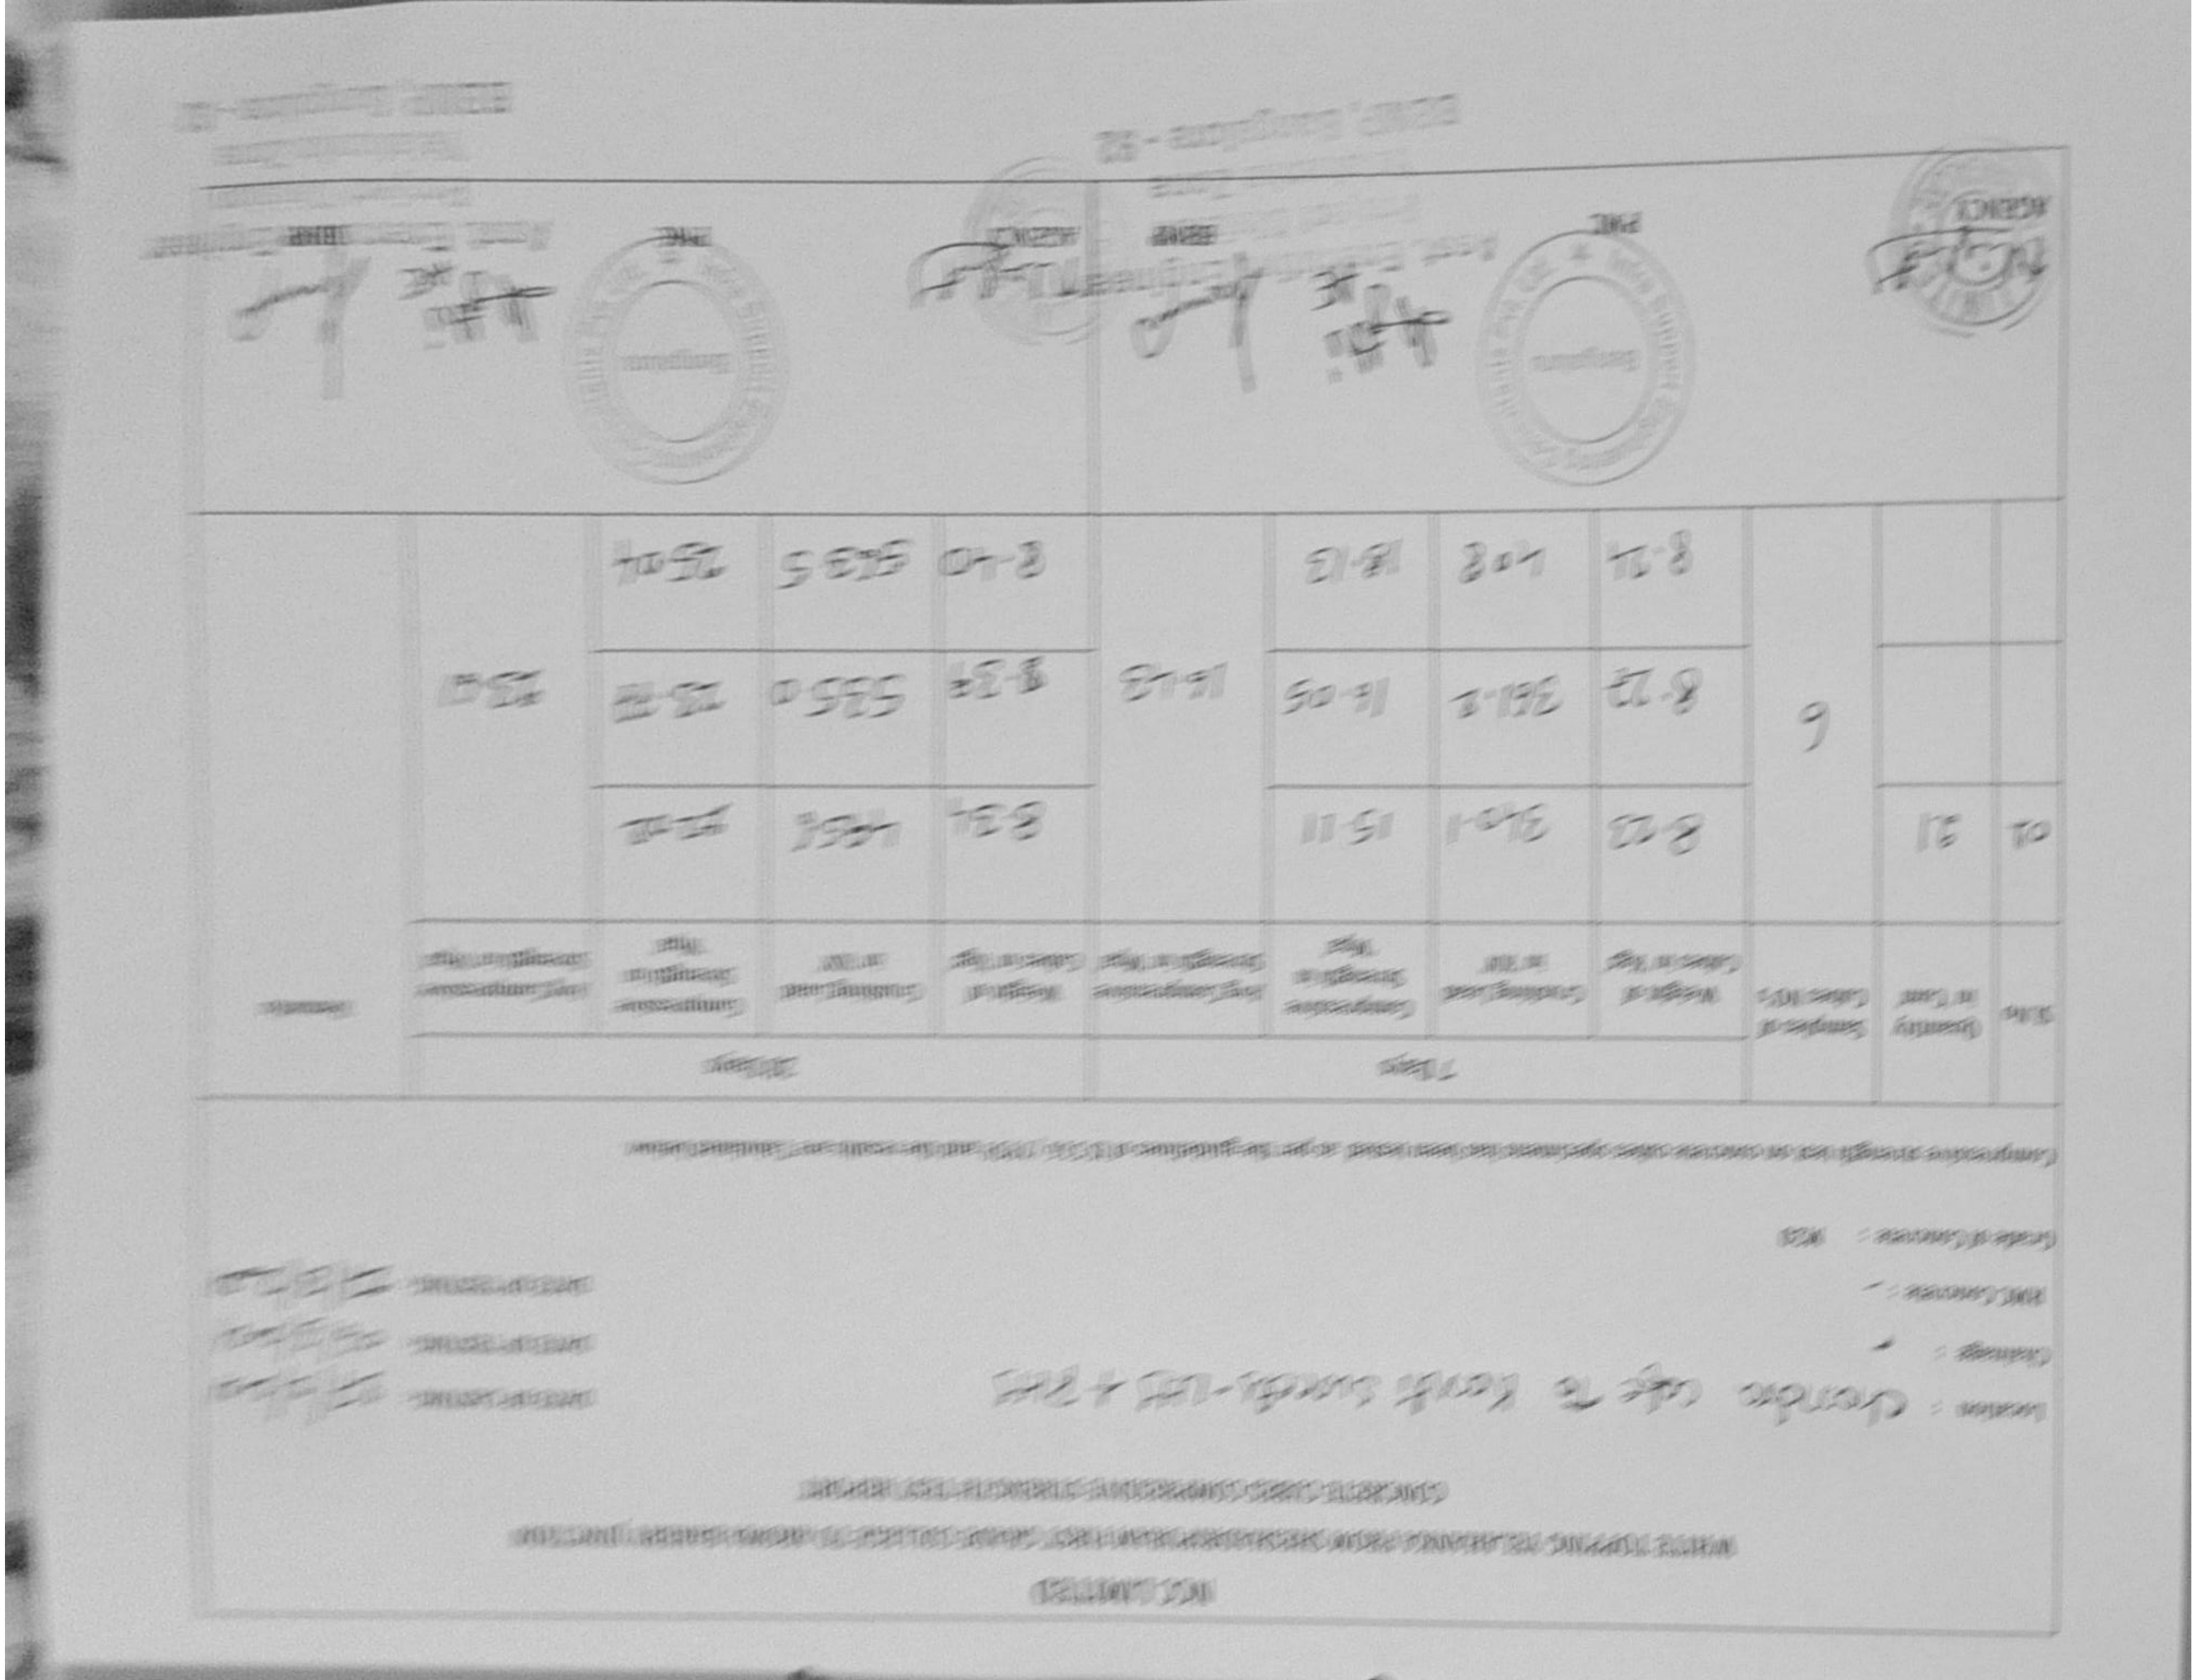

Scanned by TapScanner

NCC LIMITED

WHITE TOPPING YELAHANKA FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO AROMA BAKERY JUNCTION

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra cafe To Kanti Sweets-LHS & RHS

Chainage : -

RMC Concrete : -

Grade of Concrete : M20

DATE OF CASTING : 18/2/2021

DATE OF TESTING : 07/3/2021

DATE OF TESTING : 25/3/2021

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS 516 /1959 and the results are Tabulated below.

Sl.No	Quantity in 'Cum'	Samples of Cubes NO's	7 Days				28 Days				Remarks
			Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	
01	21	6	8.50	380.5	16.91	18.24	8.46	625.3	27.79	28.46	
			8.41	420.6	18.69		8.26	655.4	29.13		
			8.43	430.5	19.13		8.33	641.4	28.49		

AGENCY PMC AE BBMP

AGENCY PMC AE BBMP

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Scanned by TapScanner

NCC LIMITED

WHITE TOPPING YELAHANKA FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO ARKOVA BAKERY JUNCTION

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra Cafe To Kanti Sweets - LHS & RHS

Chainage : –

RMC Concrete : –

Grade of Concrete : M20

DATE OF CASTING: 3/3/2019

DATE OF TESTING: 10/3/2019

DATE OF TESTING: 31/3/2019

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS 516 : 1959 and the results are Tabulated below.

Sl.No	Quantity in 'Cum'	Samples of Cubes NO's	7 Days				28 Days				Remarks
			Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	
1	28	6	8-22	339.02	15.07	15.43	8.36	515.6	23.11	24.86	
			8-31	360	16.00		8.38	545.0	25.11		
			8-30	343.60	15.27		8.53	541	24.96		

Scanned by TapScanner

NCC LIMITED

WHITE TOPPING YELAHANKA FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO AROMA BAKERY JUNCTION

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra cafe To Kanti Sweets - LHS & RHS

Chainage : -

RMC Concrete : -

Grade of Concrete : M20

DATE OF CASTING : 4/3/2021

DATE OF TESTING : 11/3/2021

DATE OF TESTING : 01/4/2021

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS 516 /1959 and the results are Tabulated below.

Sl.No	Quantity in 'Cum'	Samples of Cubes NO's	7 Days				28 Days				Remarks
			Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	
01	12	6	8.34	373.4	16.59	16.27	8.50	476.3	21.16	21.79	
			8.28	358.2	15.92		8.49	495.1	22.00		
			8.36	366.9	16.30		8.42	500	22.22		

AGENCY

PMC

AE

BBMP

AGENCY

PMC

AE

BBMP

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Scanned by TapScanner

NCC LIMITED

WHITE TOPPING YELAHANKA FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO AROMA BAKERY JUNCTION

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra Cafe To Kanti Sweets - LHS & RHS

Chainage : -

RMC Concrete : -

Grade of Concrete : M20

DATE OF CASTING : 7/3/2021

DATE OF TESTING : 14/3/2021

DATE OF TESTING : 4/4/2021

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS 516 /1959 and the results are Tabulated below.

Sl.No	Quantity in 'Cum'	Samples of Cubes NO's	7 Days				28 Days				Remarks
			Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	
01	24	6	8.44	340	15.11	15.25	8.60	639.1	28.40	28.30	
			8.42	360	16.00		8.51	656.2	29.16		
			8.37	330	14.66		8.46	615.4	27.35		

AGENCY | PMC | AE | BBMP

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Scanned by TapScanner

NCC LIMITED

WHITE TOPPING YELAHANKA FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO AROMA BAKERY JUNCTION

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra cafe To Kanti sweets - LHS & RHS

Chainage : -

RMC Concrete : -

Grade of Concrete : M20

DATE OF CASTING : 12/3/2021

DATE OF TESTING : 19/3/2021

DATE OF TESTING : 9/4/2021

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS 516 /1959 and the results are Tabulated below.

Sl.No	Quantity in 'Cum'	Samples of Cubes NO's	7 Days				28 Days				Remarks
			Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	
01	14	6	8.19	400.3	17.79	17.95	8.28	660	29.33	29.38	
			8.26	410.7	18.25		8.35	672.5	29.88		
			8.34	400.9	17.81		8.44	651.4	28.95		

AGENCY PMC BBMP

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

AGENCY PMC BBMP

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Scanned by TapScanner

NCC LIMITED

WHITE TOPPING YELAHANKA FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO AROMA BAKERY JUNCTION

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra cafe To Kanti sweets - LHS & RHS

Chainage : -

RMC Concrete : -

Grade of Concrete : M20

DATE OF CASTING : 14/3/2021

DATE OF TESTING : 21/3/2021

DATE OF TESTING : 11/4/2021

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS 516 /1959 and the results are Tabulated below.

Sl.No	Quantity in 'Cum'	Samples of Cubes NO's	7 Days				28 Days				Remarks
			Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	
01	21	6	8.23	345	15.33	15.73	8.43	600	26.66	27.21	
			8.30	356.4	15.84		8.49	627.5	27.88		
			8.41	360.9	16.04		8.36	610	27.11		

AGENCY PMC AE BBMP AGENCY PMC AE BBMP

BBMP, Bangalore - 92

BBMP, Bangalore - 92

Scanned by TapScanner

NCC LIMITED

WHITE TOPPING YELAHANKA FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO AROMA BAKERY JUNCTION

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra Cafe To Kanti Sweets - LHS & RHS

Chainage : -

RMC Concrete : -

Grade of Concrete : M20

DATE OF CASTING : 15/3/2021

DATE OF TESTING : 22/3/2021

DATE OF TESTING : 13/4/2021

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS 516 /1959 and the results are Tabulated below.

Sl.No	Quantity in 'Cum'	Samples of Cubes NO's	7 Days				28 Days				Remarks
			Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	
01	21	6	8.42	330	14.66	15.41	8.19	505.80	22.48	23.35	
			8.48	348.9	15.50		8.22	526.3	23.39		
			8.31	362	16.08		8.30	544.2	24.18		

AGENCY

PMC

AE

BBMP

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Scanned by TapScanner

NCC LIMITED

WHITE TOPPING YELAHANKA FROM SHESHADRIPURAM FIRST CROSS JUNCTION TO HEBBAL FLYOVER (NH-7) FOR

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra Cafe To Kamki Circle - LHS & RHS

Chainage : -

RMC Concrete : -

Grade of Concrete : M20

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS:516-1959 and the results are tabulated below

Sl.No	Quantity in 'Cum'	Samples of Cubes NO's	7 Days				28 Days				Remarks
			Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	
01	24	6	8.38	375.9	16.70	18.16	8.44	458.6	20.38	23.78	
			8.32	422.8	18.79		8.51	548.1	24.36		
			8.45	422.9	19.01		8.46	614	27.30		

Engineer
BMC

Agency

Engineer
BMC

Agency

Scanned by TapScanner

WHITE TOPPING VELAHANRA FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO ARUNA BAKERY SIDE ROAD

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra Cafe To Kanthi Sweets - LHS & RHS

Chainage : -

RMC Concrete : -

Grade of Concrete : M20

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS 516 / 1959 and the results are tabulated below.

Sl.No	Quantity in 'Cum'	Samples of Cubes NO's	7 Days				28 Days				Remarks
			Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in Mpa	
1	14	6	8.43	380	16.88	17.77	8.26	561.4	24.73	23.64	
			8.46	400	17.77		8.21	524.1	23.2		
			8.22	420	18.66		8.38	554.9	24.66		

Scanned by TapScanner

CONSTRUCTION OF FLYING VELAHANKA FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO ARKHA RAMDEV JUNCTION

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra Cafe To Kardi Circle LHS & RHS

Chainage : -

RMC Concrete : -

Grade of Concrete : M20

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS:516 /1959 and the results are Tabulated below

Sl.No	Quantity in 'Cum'	Samples of Cubes NO's	7 Days				28 Days				Remarks
			Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	
01	22	6	8.18	329.9	14.66	15.78	8.31	483.2	21.47	21.91	
			8.20	356.70	15.85		8.31	492.7	21.89		
			8.25	378.7	16.83		8.42	503.3	22.57		

PMC AGENCY BBMP

PMC AGENCY BBMP

BBMP, Bangalore - 32

Scanned by TapScanner

RCC LIMITED

WHITE TOPPING YELAHANKA FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO ARUNA BAKERY JUNCTION

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra Cafe To Kanti Sweets - LHS & RHS

Chainage : -

RMC Concrete : -

Grade of Concrete : M20

DATE OF CASTING : 3/6/2014

DATE OF TESTING : 10/6/2014

DATE OF TESTING : 31/5/2014

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS 516 /1959 and the results are Tabulated below.

Sl.No	Quantity in 'Cum'	Samples of Cubes RCC's	7 Days				28 Days				Remarks
			Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	
#2	24	6	8.31	340.2	15.12	15.66	8.50	542.8	24.13	23.61	
			8.45	352	15.64		8.56	5351	23.78		
			8.50	365.2	16.23		8.48	518.6	23.04		

Scanned by TapScanner

CONSTRUCTION OF RAJA KALUVE FROM YELAHANKA TO SHESHADRIPURAM FIRST GRADE COLLEGE TO AROMA BAKERY JUNCTION

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra cafe To Kanti sweets - LHS & RHS

Chainage : -

RMC Concrete : -

Grade of Concrete : M20

DATE OF CASTING : 8/4/2021

DATE OF TESTING : 15/4/2021

DATE OF TESTING : 06/5/2021

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS 516 /1959 and the results are Tabulated below.

Sl.No	Quantity in 'Cum'	Samples of Cubes NO's	7 Days				28 Days				Remarks
			Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	
01	14	6	8.30	381.11	16.93	16.99	8.61	520.66	23.13	23.47	
			8.41	366.5	16.28		8.55	559.8	24.88		
			8.29	399.7	17.76		8.48	504.4	22.41		

AGENCY PMC BBMP

AGENCY PMC BBMP

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Scanned by TapScanner

WHITE TOPPING YELAHANKA FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO AROMA BAKERY JUNCTION

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra cafe To Kanti sweets-LHS + RHS

Chainage : -

RMC Concrete : -

Grade of Concrete : M20

DATE OF CASTING : 12/4/2021

DATE OF TESTING : 19/4/2021

DATE OF TESTING : 10/5/2021

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS 516 /1959 and the results are Tabulated below.

SLNo	Quantity in 'Cum'	Samples of Cubes NO's	7 Days				28 Days				Remarks
			Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	
01	17	6	8.51	385.70	17.44	18.0	8.31	473.80	21.05	22.02	
			8.44	409.10	18.18		8.39	495.9	22.04		
			8.48	421	18.71		8.43	517	22.97		

AGENCY PMC AE BBMP

AGENCY PMC AE BBMP

Asst Executive Engineer
Yelahanka Zone
BBMP, Bangalore - 92

Asst Executive Engineer
Yelahanka Zone
BBMP, Bangalore - 92

Scanned by TapScanner

NCC LIMITED

WHITE TOPPING RELAYING FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO ARUNACHALESHWARA JUNCTION.

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra cafe to Kamal Sweets - UP & DN

Drainage : —

RMC Concrete : —

Grade of Concrete : M30

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS516, 1959 and the results are furnished below.

Sl.No	Quantity in Cum	Samples of Cubes M/S	7 Days				28 Days				Remarks
			Weight of Cubes in Kgs	Crushing Load in KN	Compressive Strength in Mpa	Avg Compressive Strength in Mpa	Weight of Cubes in Kgs	Crushing Load in KN	Compressive Strength in Mpa	Avg Compressive Strength in Mpa	
1	22	6	8.43	364	16.06	16.04	8.40	360	16.00	35.56	
			8.20	360	16.00		8.35	360	16.00		
			8.34	345	16.10		8.45	355	34.00		

Scanned by TapScanner

NCC LIMITED

WHITE TOPPING YELAHANKA FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO AROMA BAKERY JUNCTION

CONCRETE CUBES COMPRESSIVE STRENGTH TEST REPORT

Location : Chandra Cafe To Kanti Sweets - LHS & RHS

Chainage : -

RMC Concrete : -

Grade of Concrete : M20

DATE OF CASTING : 18/4/2021

DATE OF TESTING : 25/4/2021

DATE OF TESTING : 16/5/2021

Compressive strength test on concrete cubes specimens has been tested as per the guidelines of IS 516 /1959 and the results are Tabulated below.

Sl.No	Quantity in 'Cum'	Samples of Cubes NO's	7 Days				28 Days				Remarks
			Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	Weight of Cubes in 'Kgs'	Crushing Load in 'KN'	Compressive Strength in 'Mpa'	Avg Compressive Strength in 'Mpa'	
01	30	6	8.19	427.55	19.00	18.88	8.52	522.8	23.23	23.11	
			8.21	441.10	19.60		8.40	547.8	24.34		
			8.28	406.30	18.05		8.44	490.2	21.78		

AGENCY

PMC

AE

BBMP

AGENCY

PMC

BBMP

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Asst. Executive Engineer
Project Division
BBMP, Bangalore - 92

Scanned by TapScanner

NCC LIMITED

WHITE TOPPING YELAHANKA FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO AROMA BAKERY JUNCTION

TEST REPORT

GRADATION FOR WMM
MORTH TABLE-400-II

Client : **Bruhath Bengaluru Mahanagara Palike.**

Name of Work : WHITE TOPPING YELAHANKA FROM SHESHADRIPURAM FIRST GRADE COLLEGE TO AROMA BAKERY JUNCTION

Date of Testing : 5/03/2021

Material Type : Wet Mix Macadam

Location : Chandra Cafe to Canara bank - LHS
Ch : 130 to 150

Oven Dry Wt (gm): 9283 gms

Is Sieve Size in mm	Weight Retained (gm)	Cumulative Weight Retained (gm)	Cumulative % of Retained	Cumulative % of Passing	Spec.Limits
53	0	0	0	100	100
45	223	223	2.40	97.60	95-100
22.4	2695	2918	31.48	68.57	60-80
11.2	1796	4714	50.78	49.22	40-60
4.75	1523	6237	67.18	32.82	25-40
2.36	885	7126	76.75	23.25	15-30
0.600	926	8051	86.72	13.28	8-22
0.075	1126	9177	98.85	1.15	0-5

NCCL

PMC

BBMP

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Scanned by TapScanner

Scanned by TapScanner

NCC LIMITED

[illegible]

TEST REPORT

GRADATION FOR WMM
MONTH [illegible]

Client : Bruhath Bengaluru Mahanagara Palike.
Name of Work : [illegible]
Date of Testing : 15/4/2021
Material Type : Wet Mix Macadam
Location : Chandra Layout to Vishwas pura-1st Road
Oven Dry Wt (gm): 10150 gm

IS Sieve Size in mm	Weight Retained (gm)	Cumulative Weight Retained (gm)	Cumulative % of Retained	Cumulative % of Passing	Spec Limits
53	0	0	0	100	100
45	103	158	1.34	98.66	95-100
22.4	2842	3005	29.61	70.39	60-80
11.2	1835	4840	47.68	52.32	40-60
4.75	2031	6871	67.69	32.31	25-40
2.36	842	7713	75.99	24.01	15-30
0.600	1155	8868	87.36	12.64	8-22
0.075	1032	9899	97.52	2.48	0-8

NCCL BANGALORE

PMC

AE
Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92
BBMP

Scanned by TapScanner
